
STATE PROJECT NUMBER SHEET TOTAL NO. SHEETS

GA. NHS00-0056-01(061) 115 115

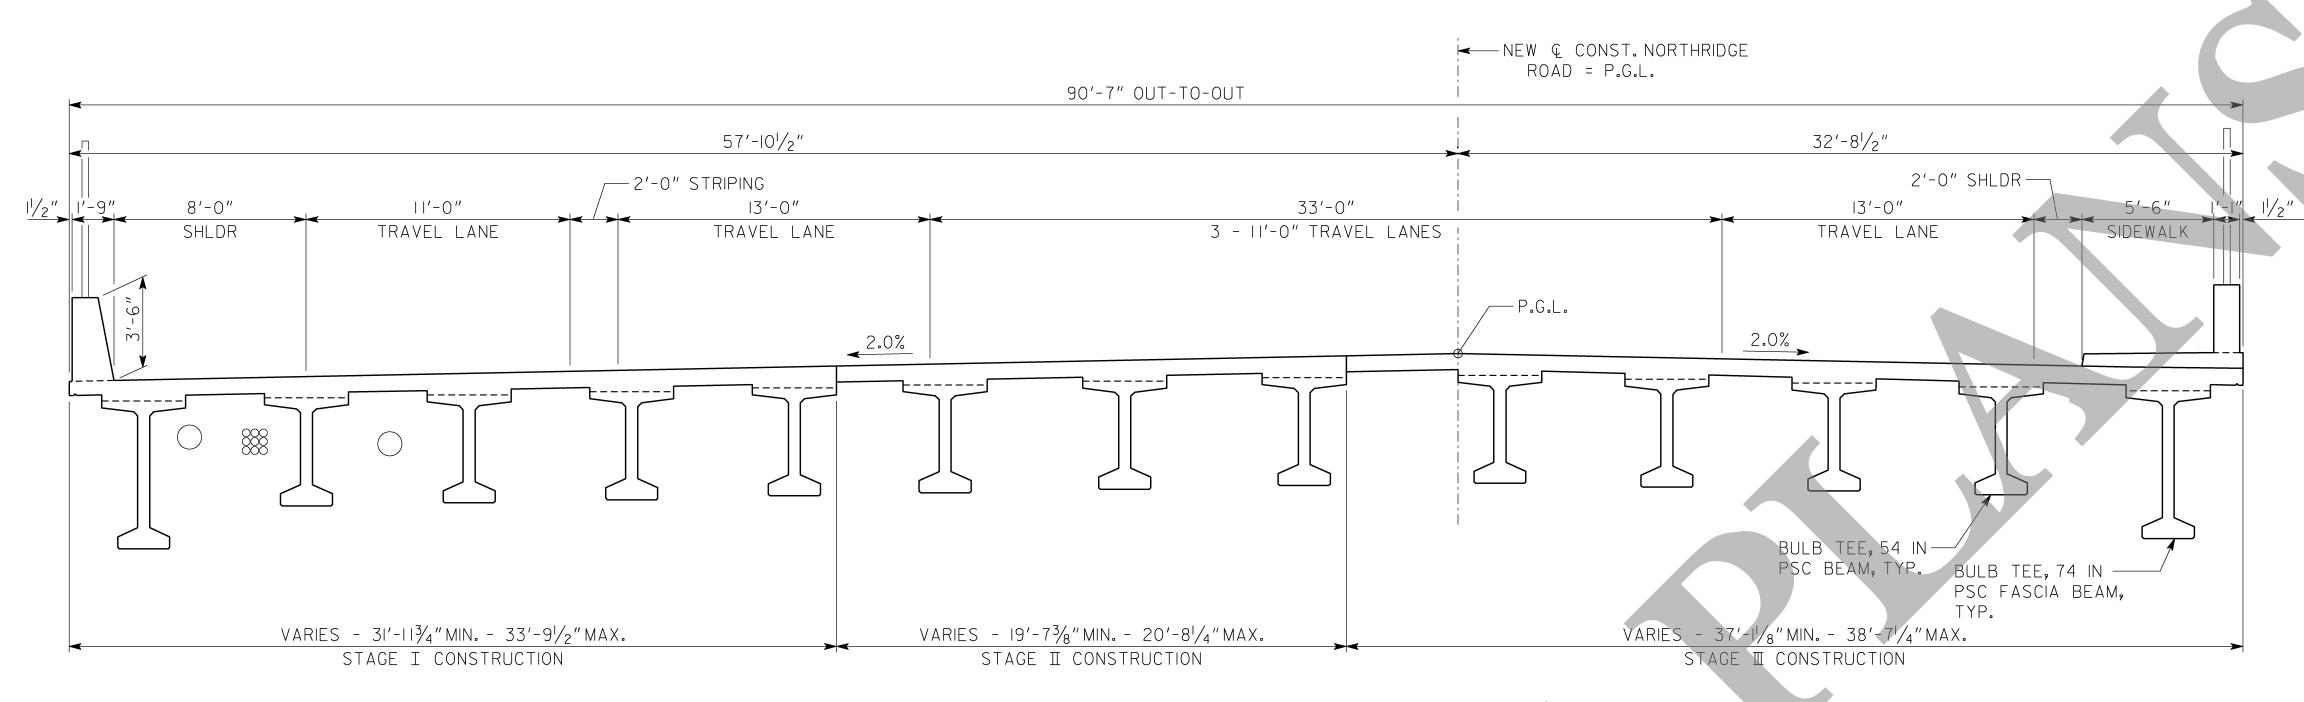

FINAL CONSTRUCTION

SPANS 2 & 3 SHOWN

(SPAN I SIMILAR)

NOTE:

I. ALL DIMENSIONS ARE RADIAL.

CONSTRUCTION SEQUENCE

<u>stage I</u> i. provide temporary shoring as needed for stage I construction.

2. BUILD STAGE I NORTH OF THE EXISTING BRIDGE ACCORDING TO THE PLANS.

3. RELOCATE WATER LINE, TELEPHONE CONDUITS, AND GAS LINE AS SHOWN ON THE PLANS.

4. PLACE TEMPORARY BARRIER "A."

<u>stage I</u> i. place temporary barrier "b." shift wb traffic to stage i construction.

2. REMOVE PORTIONS OF EXISTING BRIDGE SUPERSTRUCTURE AS SHOWN, INCLUDING SLAB AND GIRDERS. REMOVE PORTIONS OF EXISTING BRIDGE SUBSTRUCTURE AS REQUIRED, PROVIDING TEMPORARY SUPPORTS AS NECESSARY AT INTERMEDIATE BENTS.

3. PROVIDE TEMPORARY SHORING AS NEEDED FOR STAGE II CONSTRUCTION.

4. BUILD STAGE II ACCORDING TO THE PLANS.

STAGE II I. MOVE TEMPORARY BARRIER "A" AS SHOWN ON PLANS.

REMOVE TEMPORARY BARRIER "B." SHIFT EB TRAFFIC TO

STAGE I AND II CONSTRUCTION.

2. REMOVE THE REMAINING PORTIONS OF THE EXISTING BRIDGE AS SHOWN.

3. BUILD STAGE II AS SHOWN ON THE PLANS.

THE AFOREMENTIONED SEQUENCE SHALL BE COORDINATED WITH ROADWAY OPERATIONS, SEE ROADWAY PLANS. IN LIEU OF THE ABOVE CONSTRUCTION SEQUENCE, THE CONTRACTOR MAY SUBMIT A PROPOSED CONSTRUCTION SEQUENCE FOR APPROVAL.

BRIDGE NO. I



SUITE 220,2 SUN COURT NORCROSS,GA 30092-2865

GEORGIA

DATE 9/201	DEPARTMENT OF TRANSPORTATION ENGINEERING DIVISION-OFFICE OF BRIDGES AND STRUCTURES
REVISIONS TING PLAN REVISIONS	CONSTRUCTION SEQUENCE (SHEET 3 OF 3)  CR 145 (NORTHRIDGE ROAD)  OVER SR 400 (US 19)  FULTON COUNTY NHOOO-0056-01(061)

DRAWING NO.

35 - 004

BRIDGE SHEET
4 OF 4

DESIGNED AEL
DRAWN KAG
DESIGN GROUP IAB

APPROVED BFR
