


STAGE II

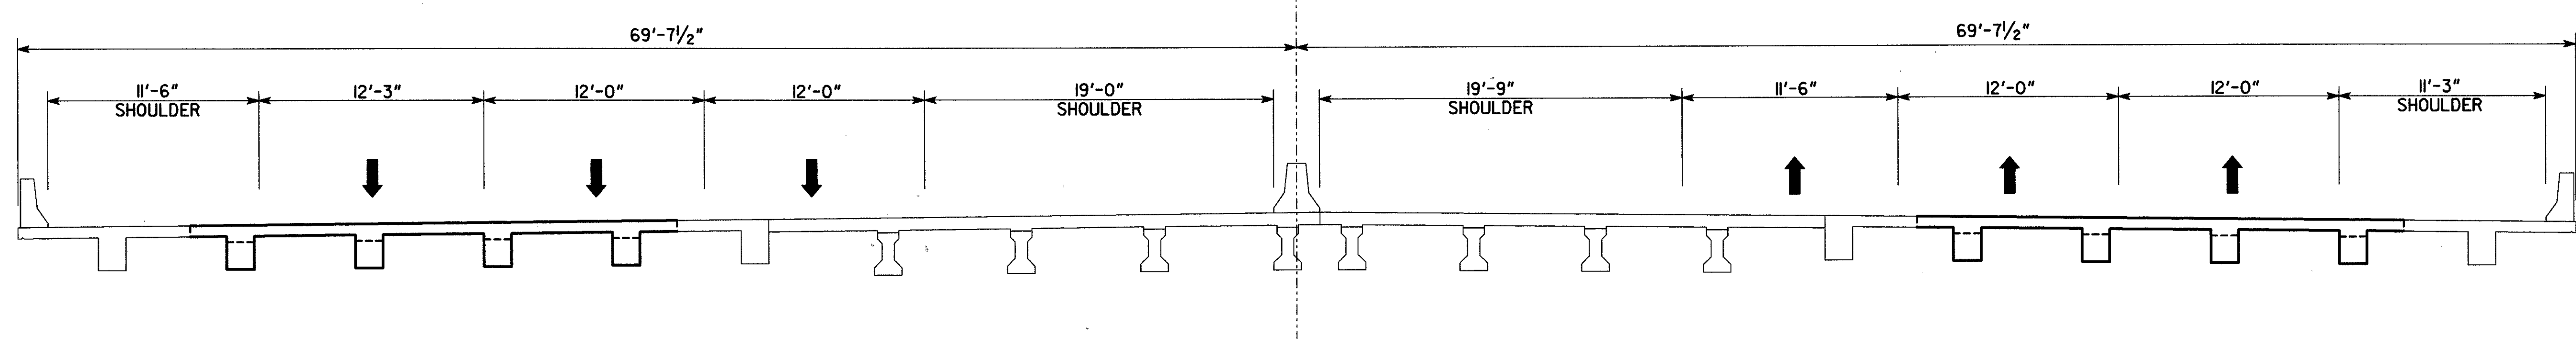

STAGE III

### STAGE CONSTRUCTION SEQUENCE

STAGE I:  
SEE ROADWAY PLANS.

STAGE II:  
1. PLACE TEMPORARY BARRIERS AT LOCATION 1 & 2.  
MAINTAIN TWO 12'-0" TRAFFIC LANES AT LOCATION SHOWN.

2. REMOVE PORTIONS OF ORIGINAL BRIDGE SUPERSTRUCTURE AND APPROACH SLABS FOR STAGE II CONSTRUCTION.

3. COMPLETE STAGE II CONSTRUCTION OF SUPERSTRUCTURE AND APPROACH SLABS.

4. CLEAN AND RESEAL EXPANSION JOINTS ENTIRE WIDTH OF BRIDGE TO THE LEFT OF TEMPORARY BARRIER LOCATION 1 AND TO THE RIGHT OF TEMPORARY BARRIER LOCATION 2.


STAGE III:  
1. REMOVE TEMPORARY BARRIERS FROM BRIDGES.

2. SHIFT TRAFFIC IN ACCORDANCE WITH STANDARD DETAIL 9106.

3. CLEAN AND RESEAL REMAINING PORTION OF EXPANSION JOINTS.

4. OPEN THE COMPLETED BRIDGE TO TRAFFIC.

THE AFOREMENTIONED SEQUENCE SHALL BE COORDINATED WITH ROADWAY PLANS. IN LIEU OF THE ABOVE SEQUENCE OF OPERATIONS, THE CONTRACTOR MAY SUBMIT A PROPOSED SEQUENCE OF OPERATIONS FOR APPROVAL.



INDICATES EXISTING STRUCTURE TO BE REMOVED AND REPLACED

BRIDGE NO. 4 LT & RT

**Heath & Lineback Engineers**  
INCORPORATED  
12 POWDER SPRINGS STREET, SUITE 240  
MARIETTA, GEORGIA 30064

GEORGIA  
**DEPARTMENT OF TRANSPORTATION**  
OPERATIONS DIVISION - OFFICE OF MAINTENANCE

CONSTRUCTION SEQUENCE  
DISTRICT 3 BRIDGE DECK REHABILITATION  
I-75 OVER FLAT CREEK  
HOUSTON COUNTY CSNHS-M002-00(783)

SCALE: NO SCALE

AUGUST 2005

BRIDGE SHEET  
3 OF 9

| DATE    | REVISIONS          |
|---------|--------------------|
| 8/26/05 | 1. CHG. CNST. SEQ. |

|              |              |              |
|--------------|--------------|--------------|
| DESIGNED TBS | CHECKED FRB  | REVIEWED GBL |
| DRAWN TBS    | DESIGN GROUP | APPROVED     |
