
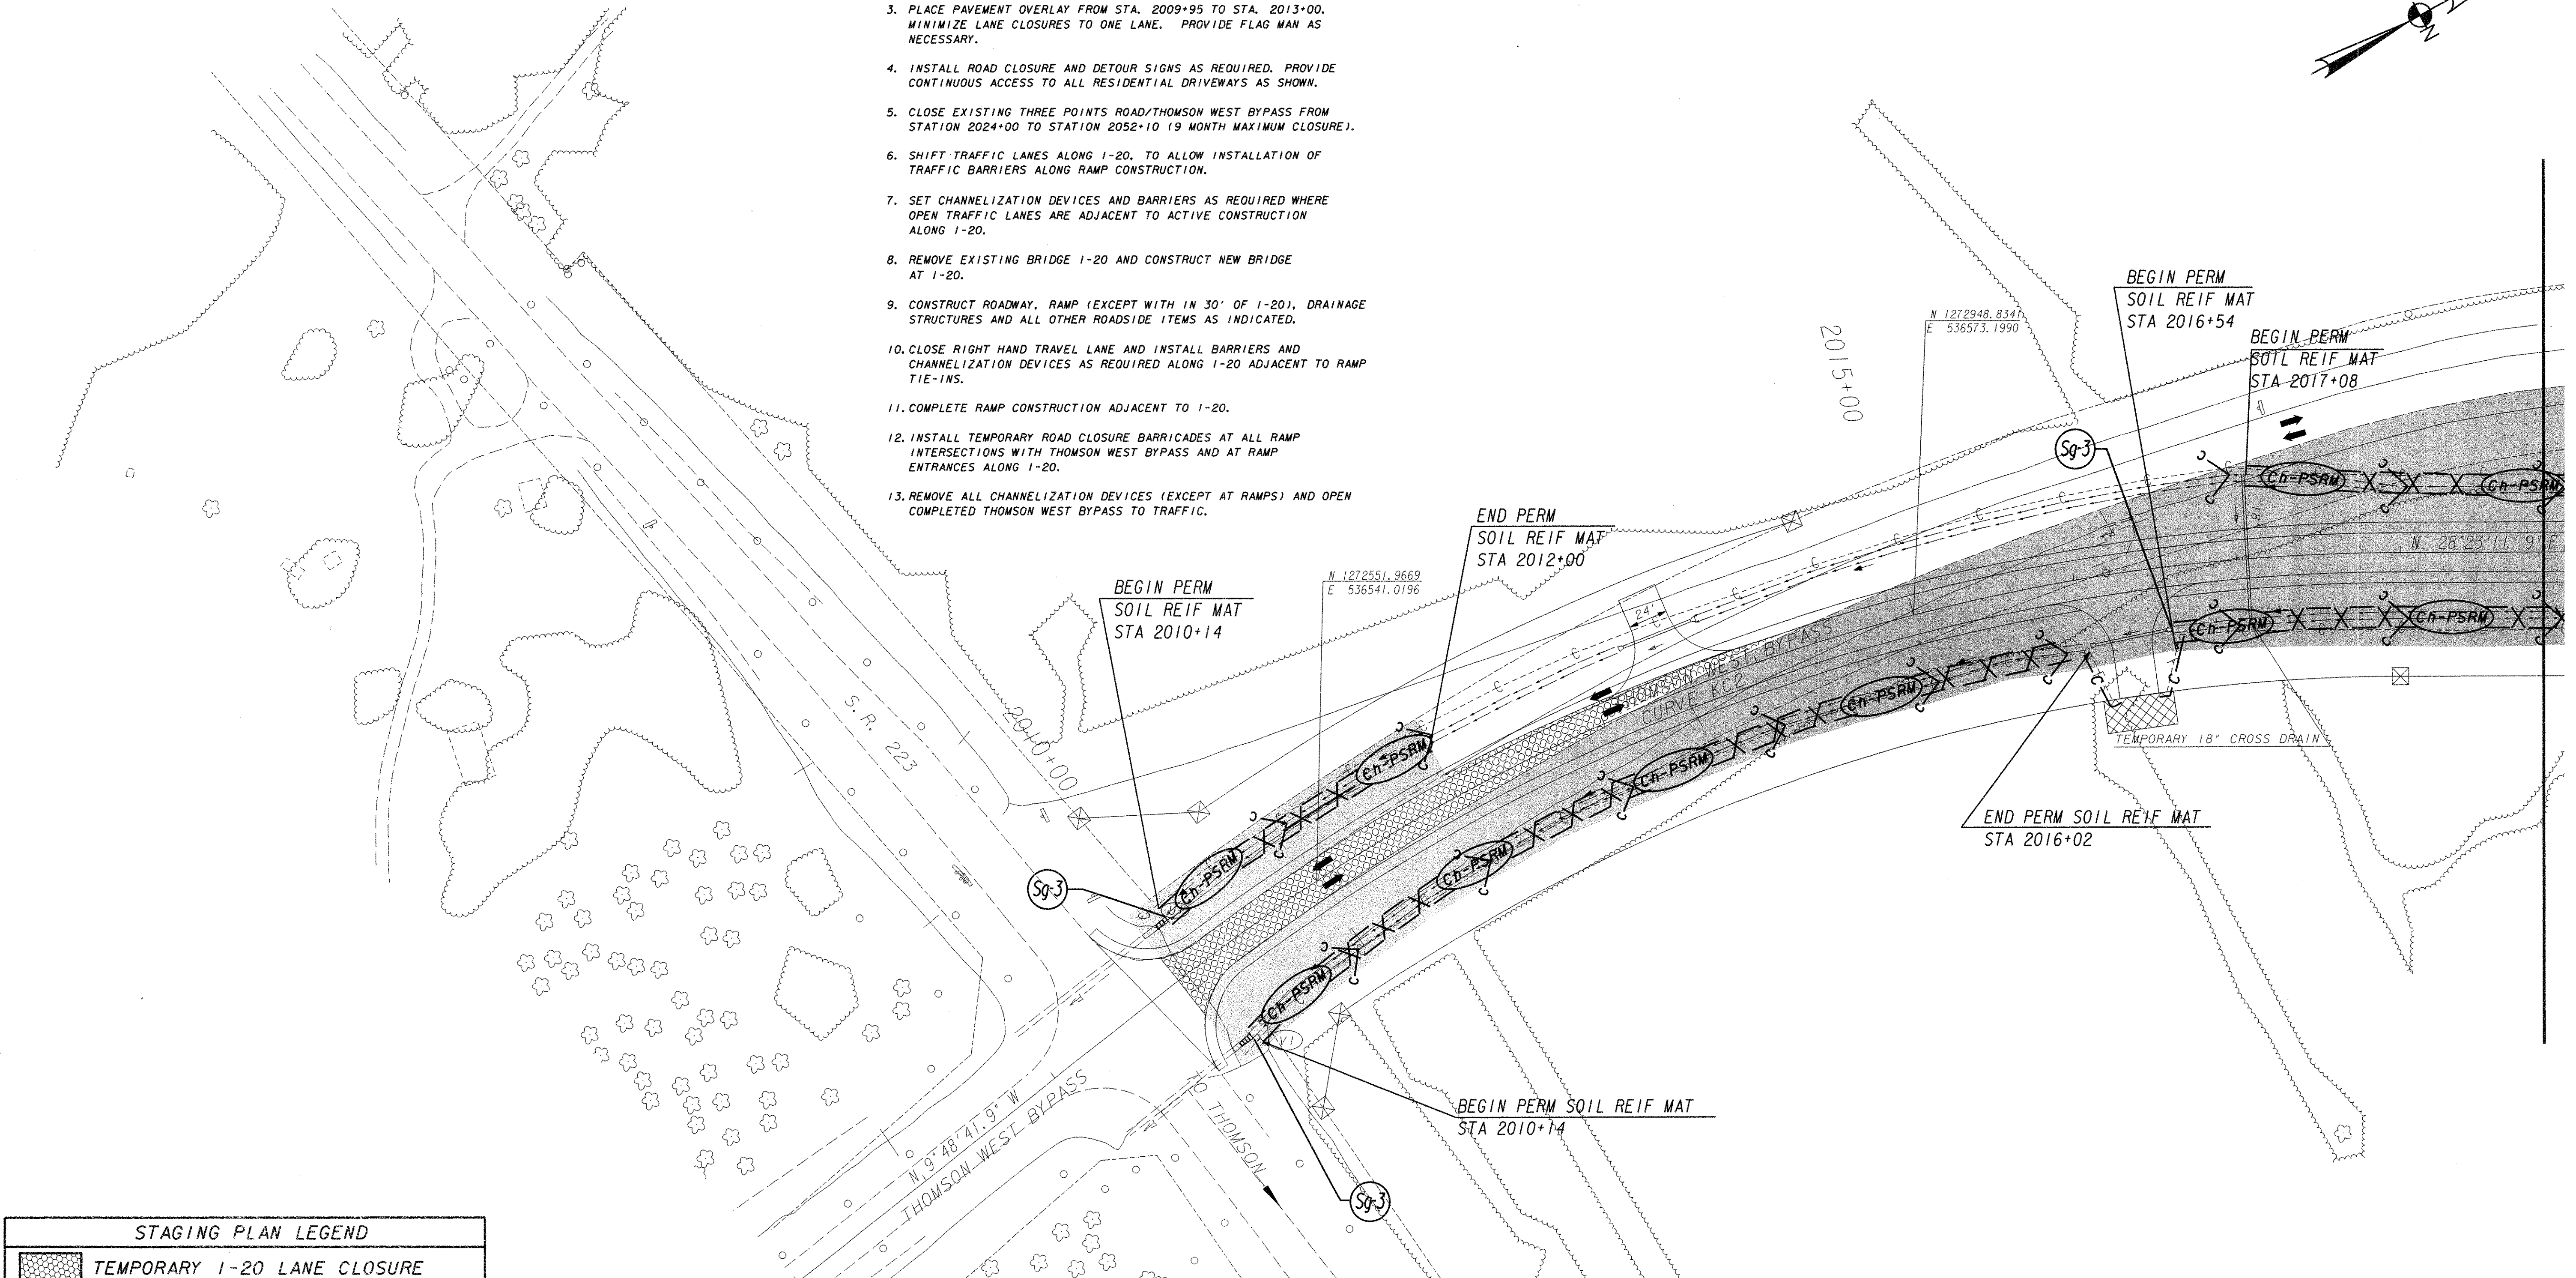



- STAGING NOTES
1. MAINTAIN TRAFFIC ON EXISTING THREE POINTS RD. TRAVEL LANES, AS INDICATED.
 2. SET CHANNELIZATION DEVICES AND BARRIERS AS REQUIRED WHERE OPEN TRAFFIC LANES ARE ADJACENT TO ACTIVE CONSTRUCTION ALONG THREE POINTS RD./THOMSON WEST BYPASS.
 3. PLACE PAVEMENT OVERLAY FROM STA. 2009+95 TO STA. 2013+00. MINIMIZE LANE CLOSURES TO ONE LANE. PROVIDE FLAG MAN AS NECESSARY.
 4. INSTALL ROAD CLOSURE AND DETOUR SIGNS AS REQUIRED. PROVIDE CONTINUOUS ACCESS TO ALL RESIDENTIAL DRIVEWAYS AS SHOWN.
 5. CLOSE EXISTING THREE POINTS ROAD/THOMSON WEST BYPASS FROM STATION 2024+00 TO STATION 2052+10 (9 MONTH MAXIMUM CLOSURE).
 6. SHIFT TRAFFIC LANES ALONG I-20, TO ALLOW INSTALLATION OF TRAFFIC BARRIERS ALONG RAMP CONSTRUCTION.
 7. SET CHANNELIZATION DEVICES AND BARRIERS AS REQUIRED WHERE OPEN TRAFFIC LANES ARE ADJACENT TO ACTIVE CONSTRUCTION ALONG I-20.
 8. REMOVE EXISTING BRIDGE I-20 AND CONSTRUCT NEW BRIDGE AT I-20.
 9. CONSTRUCT ROADWAY, RAMP (EXCEPT WITH IN 30' OF I-20), DRAINAGE STRUCTURES AND ALL OTHER ROADSIDE ITEMS AS INDICATED.
 10. CLOSE RIGHT HAND TRAVEL LANE AND INSTALL BARRIERS AND CHANNELIZATION DEVICES AS REQUIRED ALONG I-20 ADJACENT TO RAMP TIE-INS.
 11. COMPLETE RAMP CONSTRUCTION ADJACENT TO I-20.
 12. INSTALL TEMPORARY ROAD CLOSURE BARRICADES AT ALL RAMP INTERSECTIONS WITH THOMSON WEST BYPASS AND AT RAMP ENTRANCES ALONG I-20.
 13. REMOVE ALL CHANNELIZATION DEVICES (EXCEPT AT RAMP) AND OPEN COMPLETED THOMSON WEST BYPASS TO TRAFFIC.

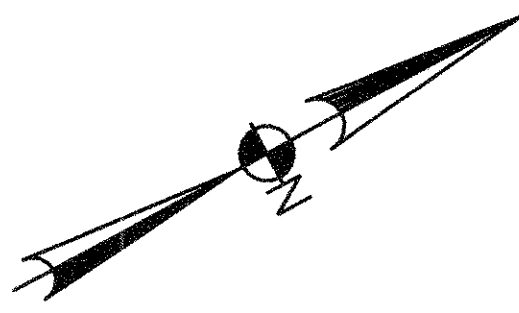

MATCH LINE STA. 2019+00
SEE SHEET 54-10

STAGING PLAN LEGEND					
	TEMPORARY I-20 LANE CLOSURE				
	PERMANENT CONSTRUCTION/PAVEMENT				
	STAGED OVERLAY				
	TEMPORARY CONCRETE BARRIERS				
	TEMPORARY SAND LOADED MODULES				
	TRAFFIC THIS STAGE				

STAGE 2A BMP LOCATION DETAILS



REVISIONS					
Δ	DATE	BY	DESCRIPTION	Δ	DATE

MA Moreland Altabelli Associates Inc.
2211 Beaver Run Road
Suite 190
Norcross, Georgia 30071
Telephone (770) 263-5945

DESIGNED BY	NAME	DATE	DRAWN BY	NAME	DATE	QUANTITIES BY	NAME	DATE
CHECKED BY			CHECKED BY			CHECKED BY		
SUPERVISED BY								
