



WORK DESCRIPTION
 CLEARING AND GRUBBING, AND DEMOLITION

PRIOR TO CLEARING AND GRUBBING IN PHASE 1 OF THE PROJECT THE CONTRACTOR SHALL PLACE TYPE C SILT FENCE WITH A MUD BERM AROUND THE SITE WHERE DEPICTED ON PLANS AND INSTALL THE NECESSARY CONSTRUCTION EXIT. ONCE EROSION AND SEDIMENT CONTROL MEASURES ARE IN PLACE, THE CLEARING AND GRUBBING MAY COMMENCE. MULCH SHOULD BE USED TO STABILIZE ANY AREAS LEFT DISTURBED FOR MORE THAN 7 DAYS. A TEMPORARY SEDIMENT BASIN SHALL BE CONSTRUCTED. TEMPORARY SEEDING AND DUST CONTROL SHOULD ALSO BE PROVIDED FOR ANY DISTURBED AREAS. APPROXIMATELY 8.65 ACRES WILL BE DISTURBED IN PHASE 1. REFER TO SHEET 51-02 FOR EROSION CONTROL CALCULATIONS.


TOTAL SITE AREA = 9.64 ACRES

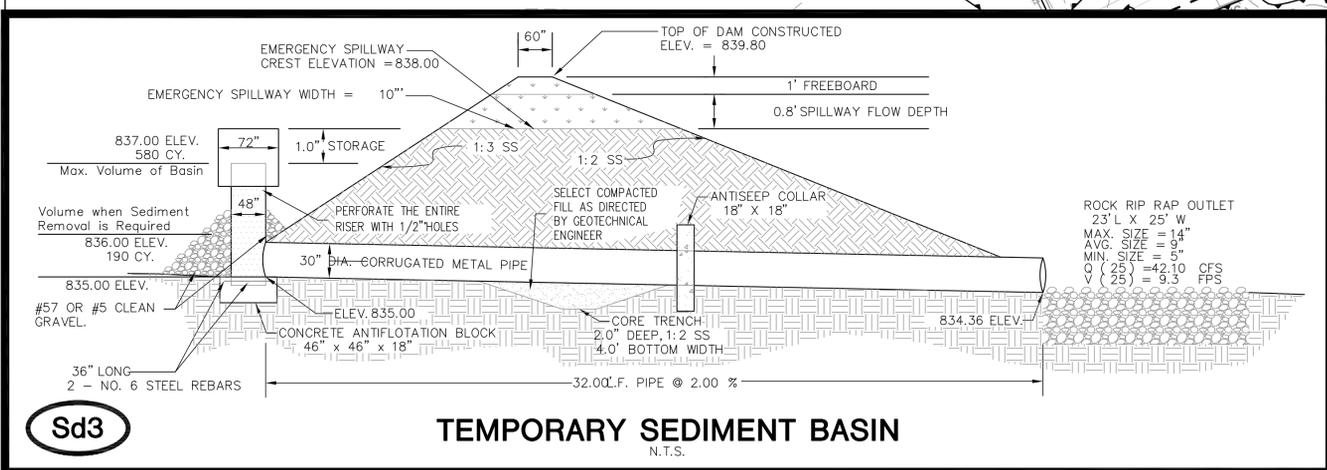

Sd3
TEMPORARY SEDIMENT BASIN
 N.T.S.



URS
 400 Northpark Town Center
 1000 Abernathy Road N.E., Suite 900
 Atlanta, Georgia 30328
 Tel: (678) 808-8800, Fax: (678) 808-8400



REVISIONS	
05/07/2010	

STATE OF GEORGIA
 DEPARTMENT OF TRANSPORTATION
 OFFICE OF INNOVATIVE PROGRAM DELIVERY
ESPCP BMP LOCATION DETAILS
STAGE 1

NEWMAN SR 34 AND HOLLZ PKWY
 PARK AND RIDE LOT

54-01
 DRAWING No.
