



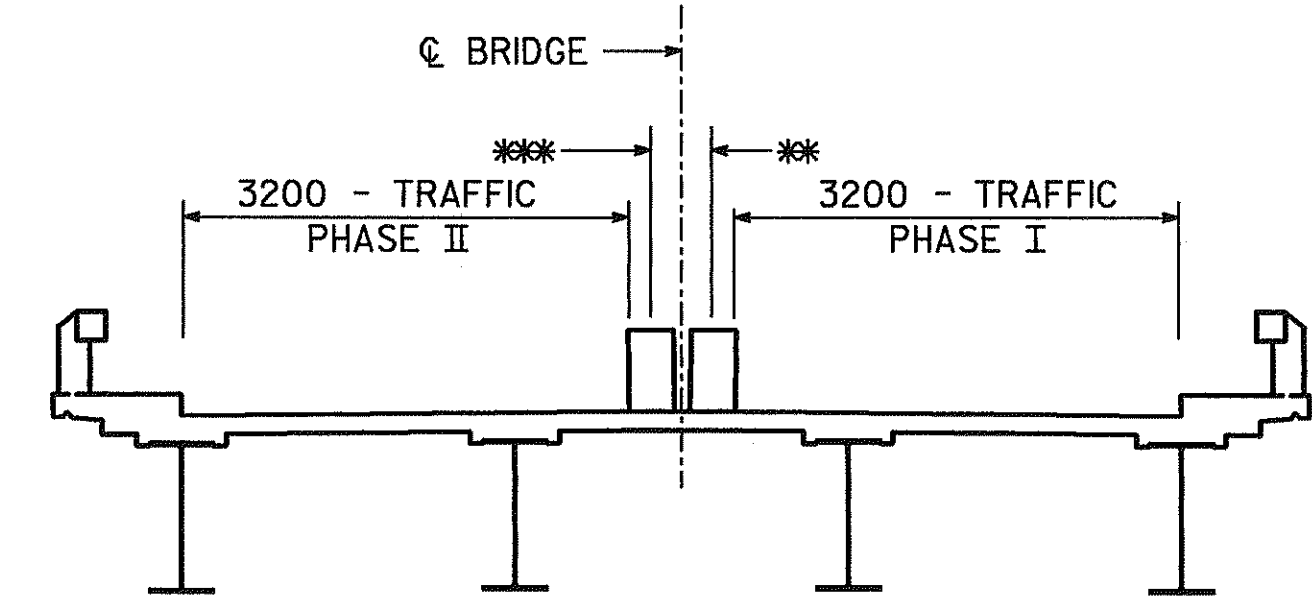


STATE	PROJECT NUMBER	SHEET NO.	TOTAL SHEETS
GA.	IM-STP-00MS(265)	12	198

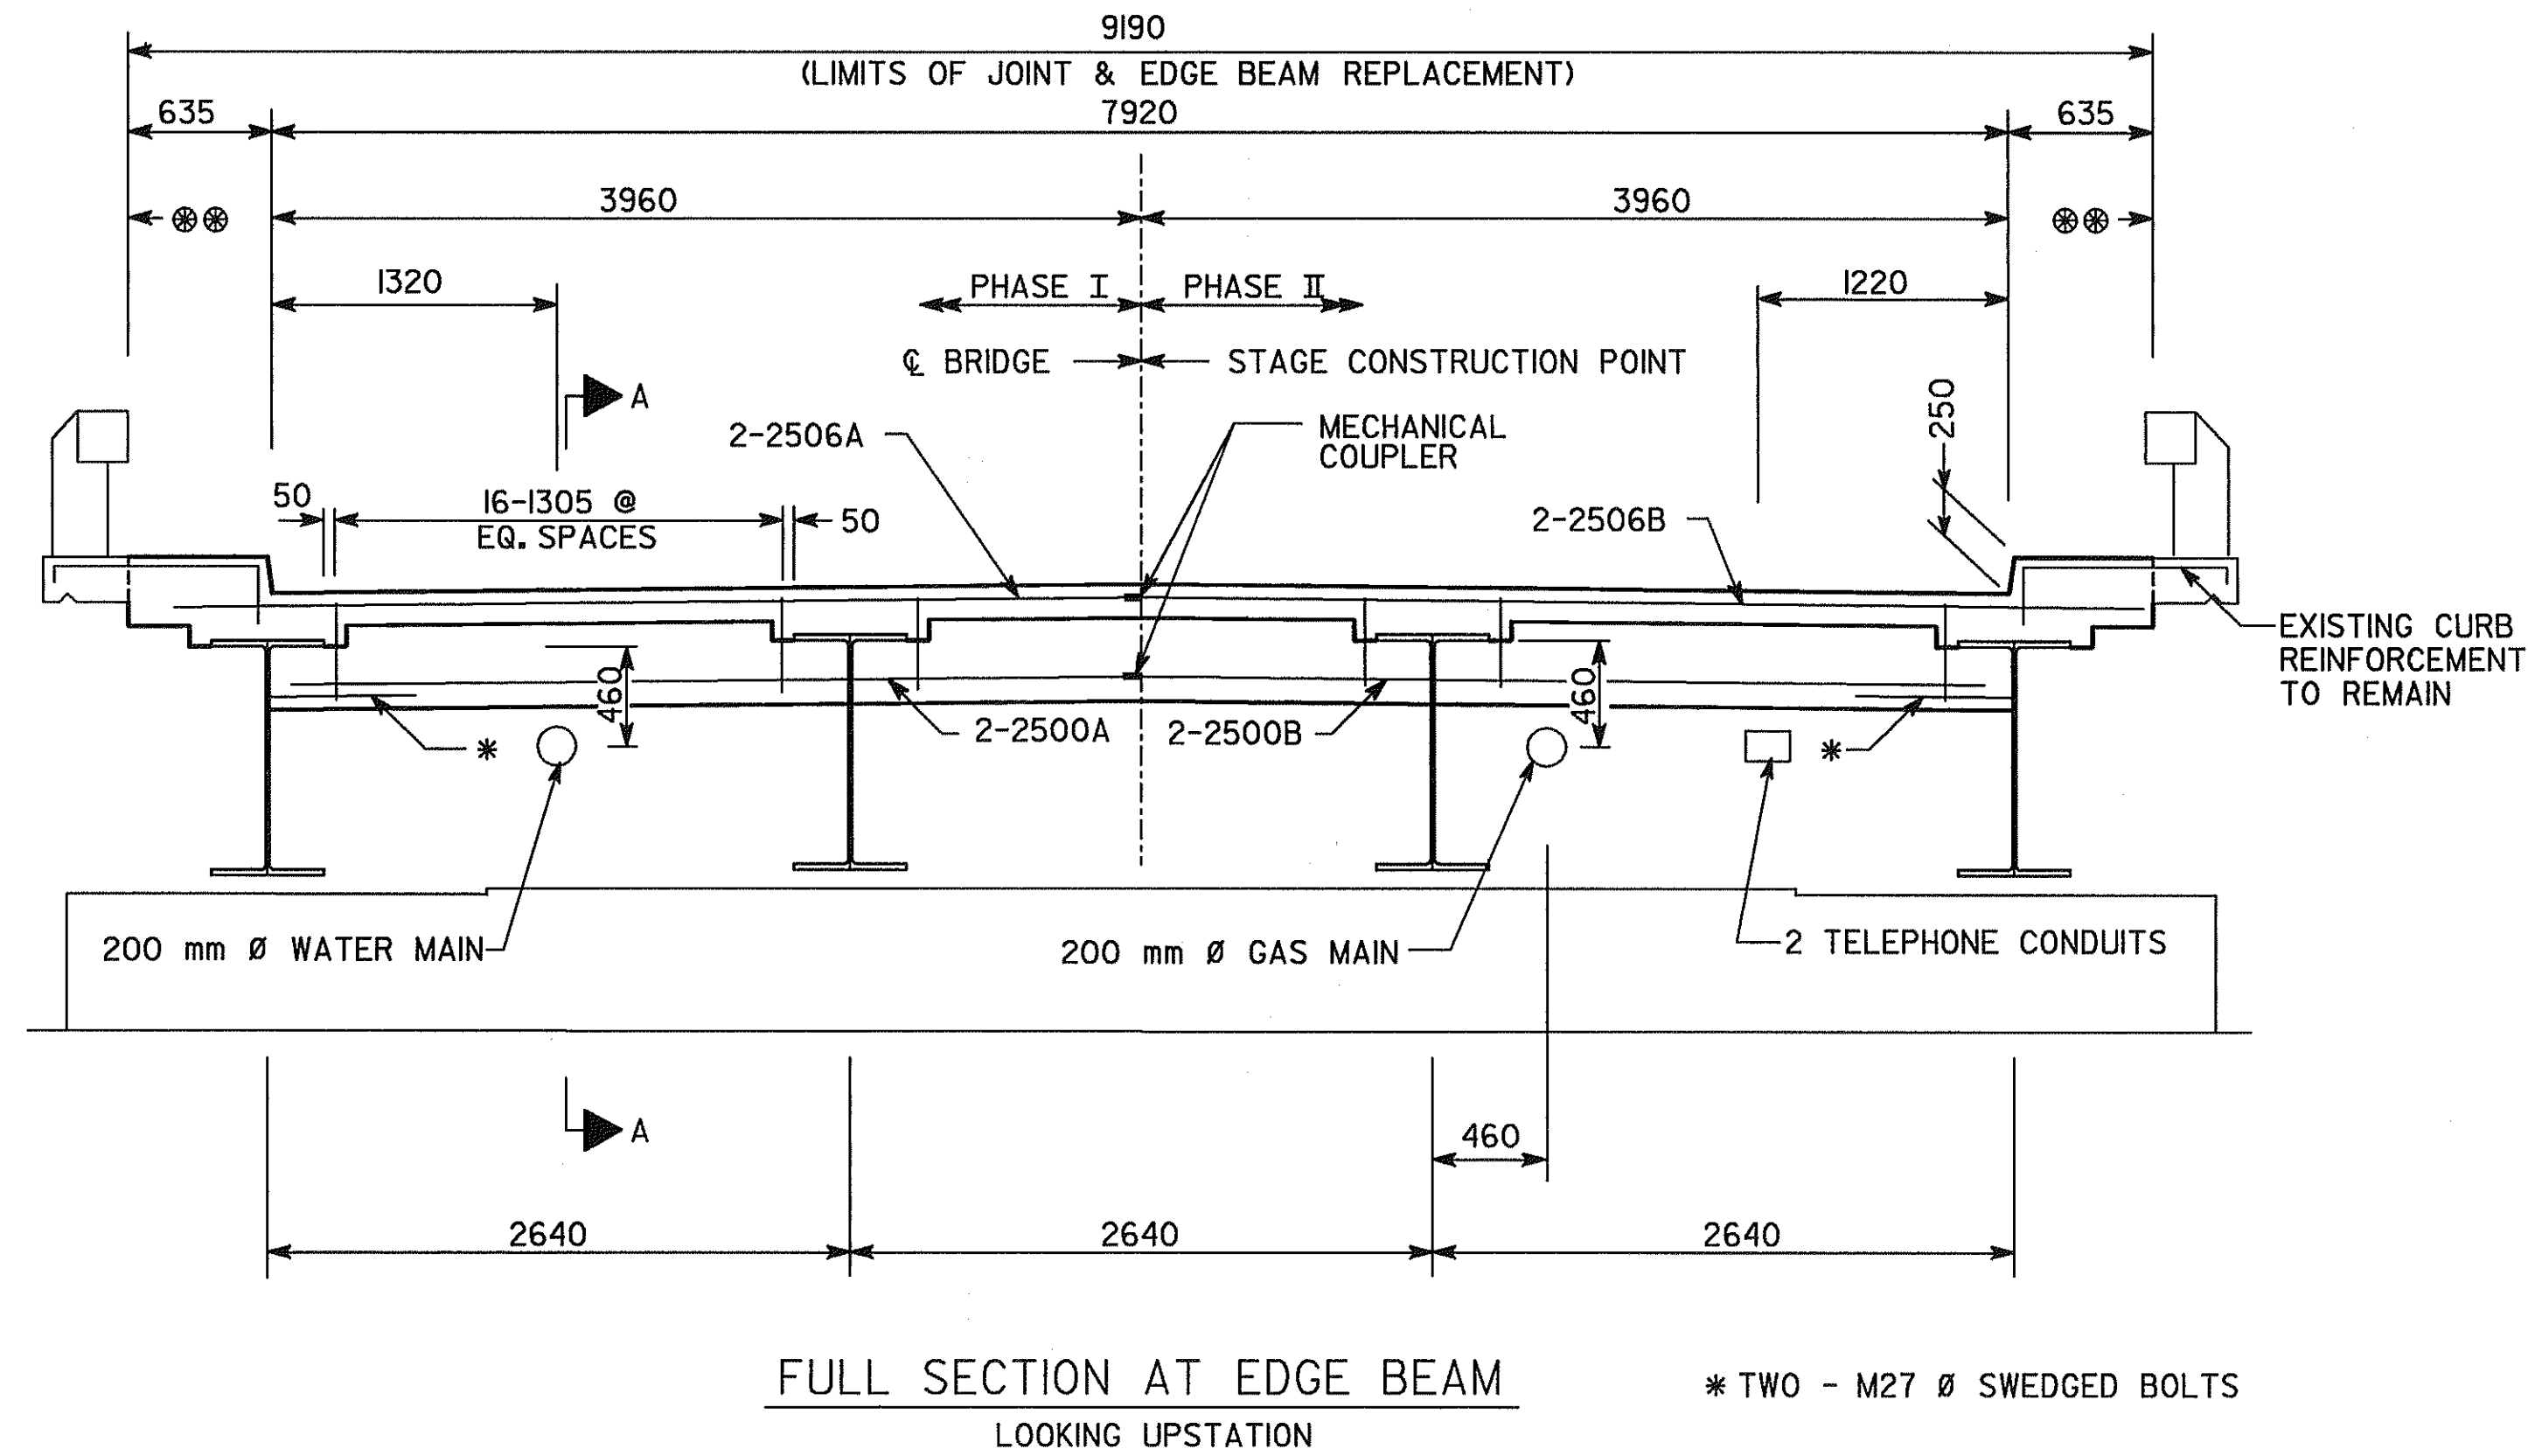

CONSTRUCTION SEQUENCE  
LOOKING UPSTATION


\*\*- PHASE I TEMP. CONSTRUCTION BARRIER LOCATION  
\*\*\* - PHASE II TEMP. CONSTRUCTION BARRIER LOCATION

1. PLACE STRIPED DRUMS AT PHASE I LOCATION, MAINTAINING ONE 3200 mm TRAVEL LANE ON BRIDGE.
2. REMOVE PARTS OF EXISTING BRIDGE, BUILD PHASE I ACCORDING TO THE PLANS.
3. RELOCATE STRIPED DRUMS TO PHASE II LOCATION, MAINTAINING ONE 3200 mm TRAVEL LANE ON BRIDGE.
4. REMOVE PARTS OF EXISTING BRIDGE, BUILD PHASE II ACCORDING TO THE PLANS.
5. REMOVE STRIPED DRUMS AND OPEN COMPLETED BRIDGE TO TRAFFIC.

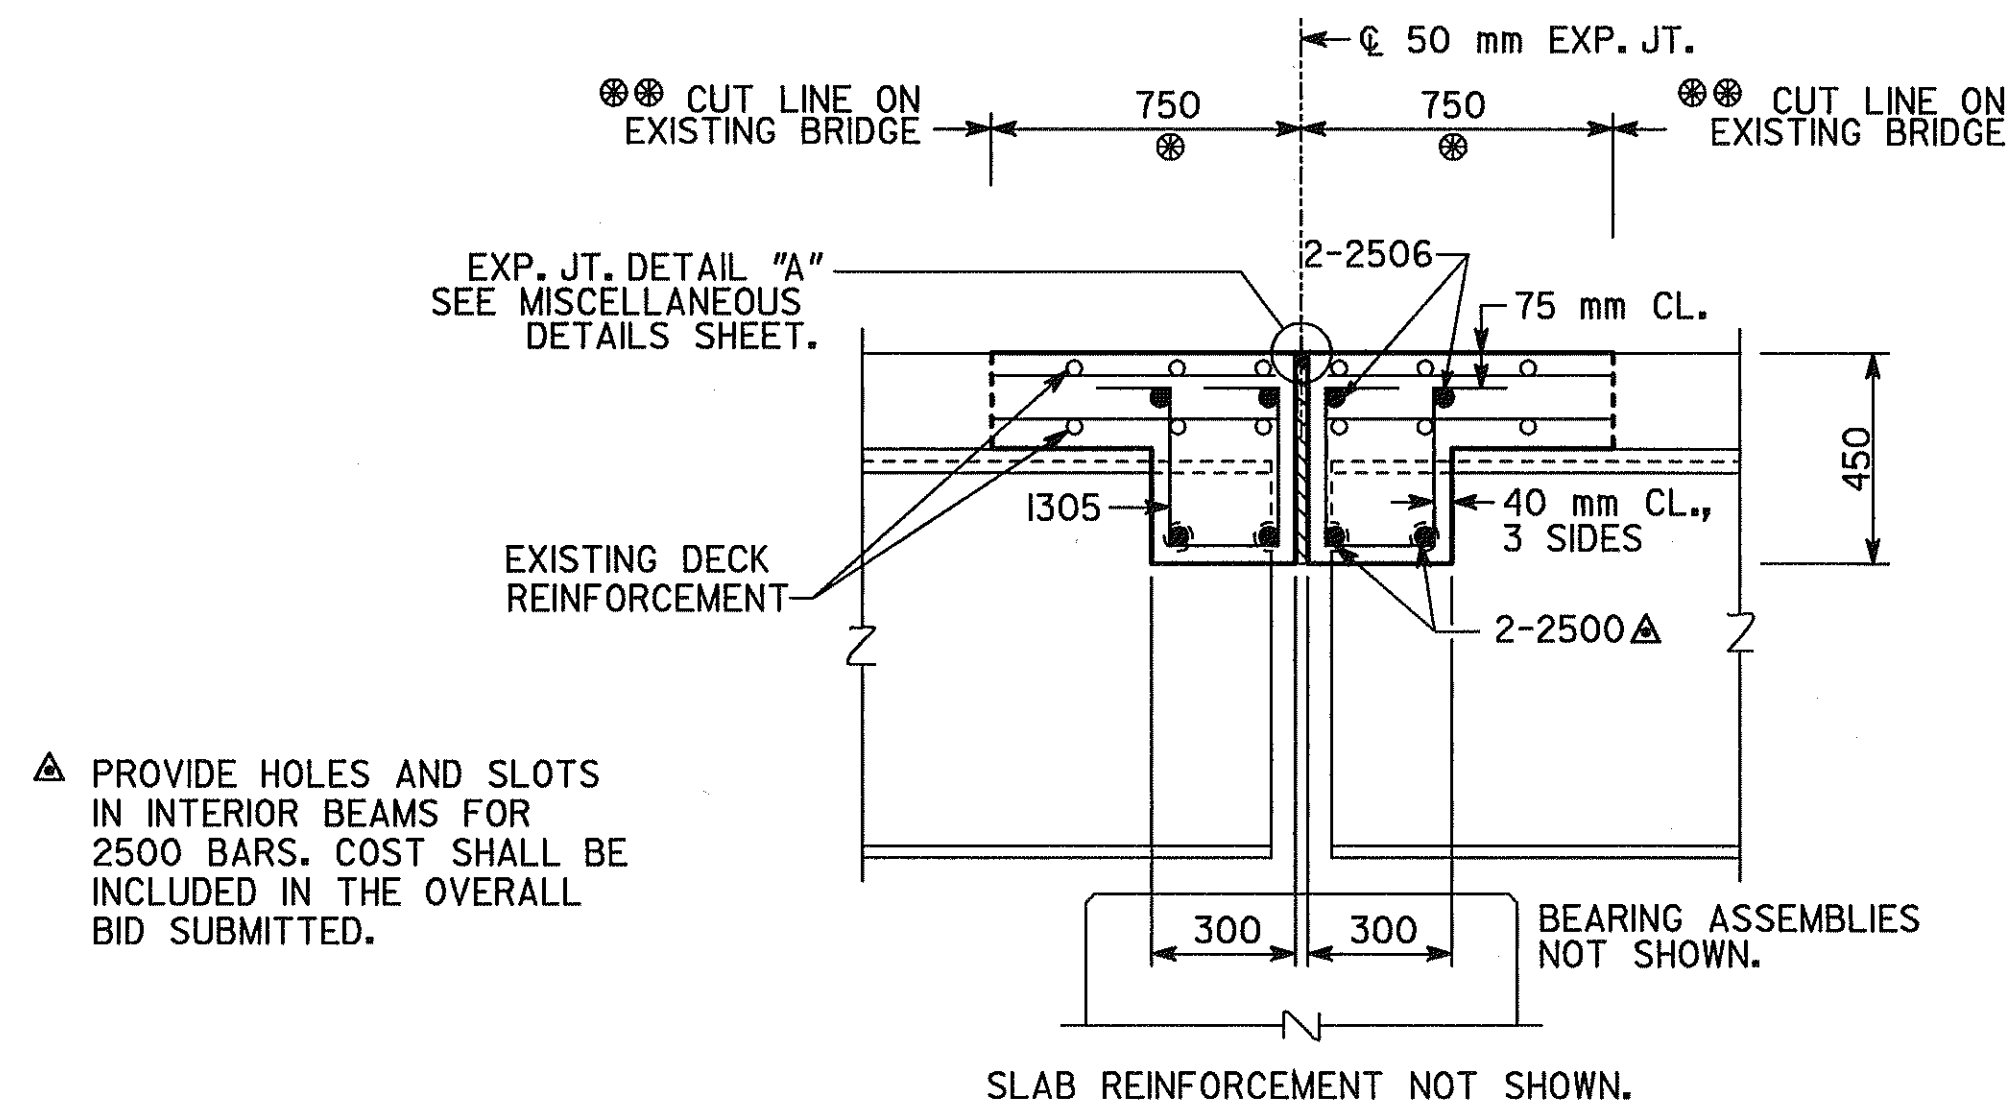


SECTION A-A THRU EDGE BEAM @ BENT 3

- NOTES: EXISTING DECK, AND CURB REINFORCEMENT TO REMAIN. REINFORCING STEEL DAMAGED BY CONTRACTOR SHALL BE REPLACED AT NO COST TO THE DEPARTMENT.
- ⊗ PORTION OF DECK, CURB, EDGE BEAM AND BACKWALL TO BE REMOVED AND REPLACED AS SHOWN.
  - ⊗ REQUIRED VERTICAL 25 mm SAW CUT. CARE SHALL BE EXERCISED SO THAT THE EXISTING REINFORCING STEEL IS NOT DAMAGED.

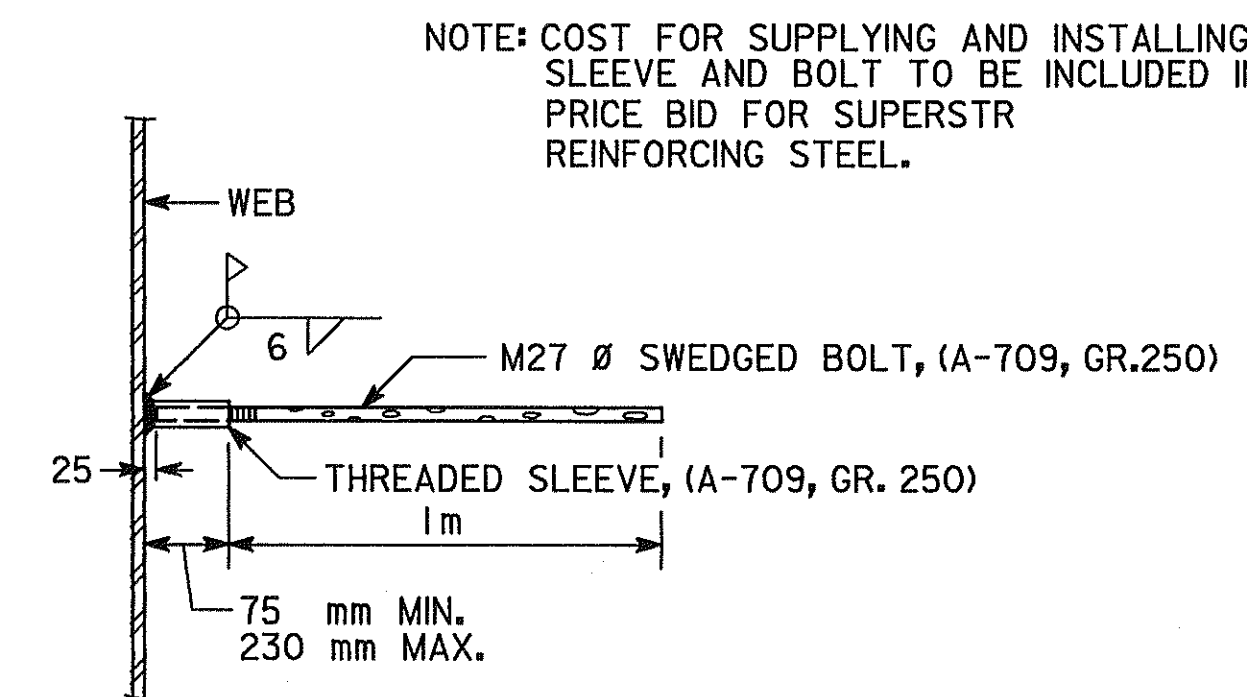

EDGE BEAM BAR LAP DETAIL  
NOT TO SCALE

BRIDGE NO. 1



GEORGIA  
DEPARTMENT OF TRANSPORTATION  
PRECONSTRUCTION DIVISION-OFFICE OF MAINTENANCE

SUPERSTRUCTURE DETAIL & CONST. SEQ.  
JOINT & EDGE BEAM REPLACEMENT ON  
FIELDER ROAD (C.R. 134) OVER I-75

CLAYTON COUNTY, GA. IM-STP-00MS(265)

SCALE: NO SCALE DECEMBER 1999

BRIDGE SHEET	DESIGNED	CHECKED	REVIEWED
3 OF 4	GW	CAD	
		DESIGN GROUP MAINTENANCE	APPROVED
