STAGE CONSTRUCTION

STAGE 1

1. MAINTAIN TRAFFIC ON EXISTING SR 119
2. COMPLETE PROPOSED CONSTRUCTION UP TO ASPHALT BINDER
3. MAINTAIN ACCESS TO DRIVEWAYS WHERE DIRECTED BY ENGINEER.
4. PLACE LEVELING ON EXISTING SR 119 AS NEEDED TO MAINTAIN POSITIVE DRAINAGE (PERMANENT & TEMPORARY MAY BE NEEDED).
5. INSTALL DRAINAGE AS NEEDED TO MAINTAIN POSITIVE DRAINAGE.

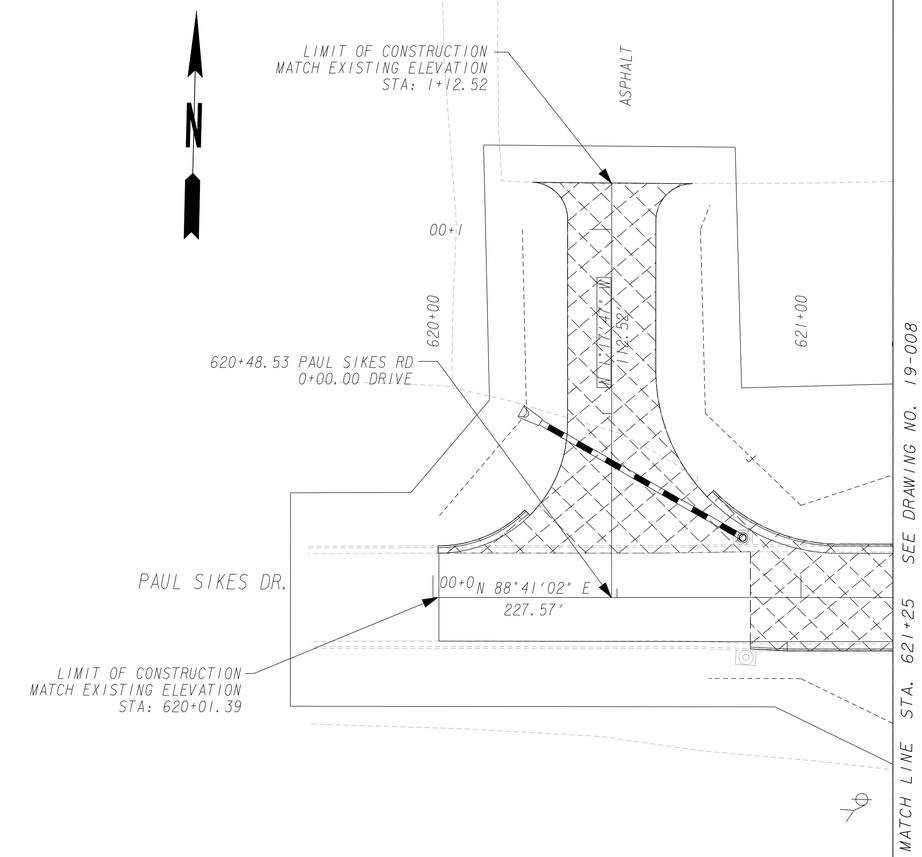

LEGEND

- PAVEMENT REMOVAL
- TEMPORARY CONSTRUCTION PAVEMENT
- PERMANENT CONSTRUCTION
- CONCRETE MEDIAN CONSTRUCTION
- MILL & OVERLAY CONSTRUCTION
- OPEN LANES OF TRAFFIC

PROPERTY AND EXISTING R/W LINE
REQUIRED R/W LINE
CONSTRUCTION LIMITS
EASEMENT FOR CONSTR & MAINTENANCE OF SLOPES
EASEMENT FOR CONSTR OF SLOPES
EASEMENT FOR CONSTR OF DRIVES

BEGIN LIMIT OF ACCESS.....BLA
END LIMIT OF ACCESS.....ELA
LIMIT OF ACCESS
REQ'D R/W & LIMIT OF ACCESS

THOMAS & HUTTON ENGINEERING CO.
50 PARK OF COMMERCE WAY
P.O. BOX 2727
SAVANNAH, GA 31402
PHONE: (912) 234-5300
FAX: (912) 234-2950
WWW.THOMAS-HUTTON.COM
GEORGIA - SAVANNAH, BRUNSWICK
SOUTH CAROLINA - CHARLESTON, MYRTLE BEACH
NORTH CAROLINA - WILMINGTON

SCALE IN FEET
0 20 40 80

REVISION DATES

STATE OF GEORGIA
DEPARTMENT OF TRANSPORTATION
OFFICE: PROGRAM DELIVERY

CONSTRUCTION STAGING PLAN

S.R. 119 Liberty Co.
STAGE 1

DRAWING No. 19-036

3/1/2007 GPLN
