DATETIME$$$	TIME$$$	PRF	DGN	COUNTY	PROJECT NUMBER	SHEET NO.	TOTAL SHEETS
$USER$		$$PENTABLE$$		FULTON	NH000-0085-02(153)	165	396

CONTROL ACQUIRED BY GPS OR LOCAL SURVEY PROVIDED BY: TBE GROUP, INC.
HORIZONTAL DATUM: NAD'83(94 HARN)
VERTICAL DATUM: NAVD'88
UTILITY IN CONFLICT: UNKNOWN SIZE/TYPE BURIED TELEPHONE
UTILITIES FOUND: 2½" STEEL CONDUIT BURIED TELEPHONE
CONDITION OF UTILITY(OBSERVED): GOOD
FIELD CONDITION: TALL GRASS
PAVING THICKNESS AND TYPE: N/A
CONDITION OF PAVING PRIOR TO WORK: N/A
PORTION OF PIPE EXPOSED FOR O.D. MEASUREMENT: FULL
REMARKS: N/A

CROSS SECTIONAL VIEW (FACING NORTHEAST)

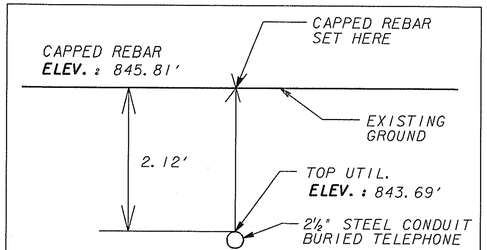

(TEST HOLE COORDS.)
N: 1391037.88
E: 2238862.85

NOTE: DEPTHS SHOWN WERE MEASURED, NOT CALCULATED.

SCALE IN FEET
0 50 100 150

PLAN VIEW

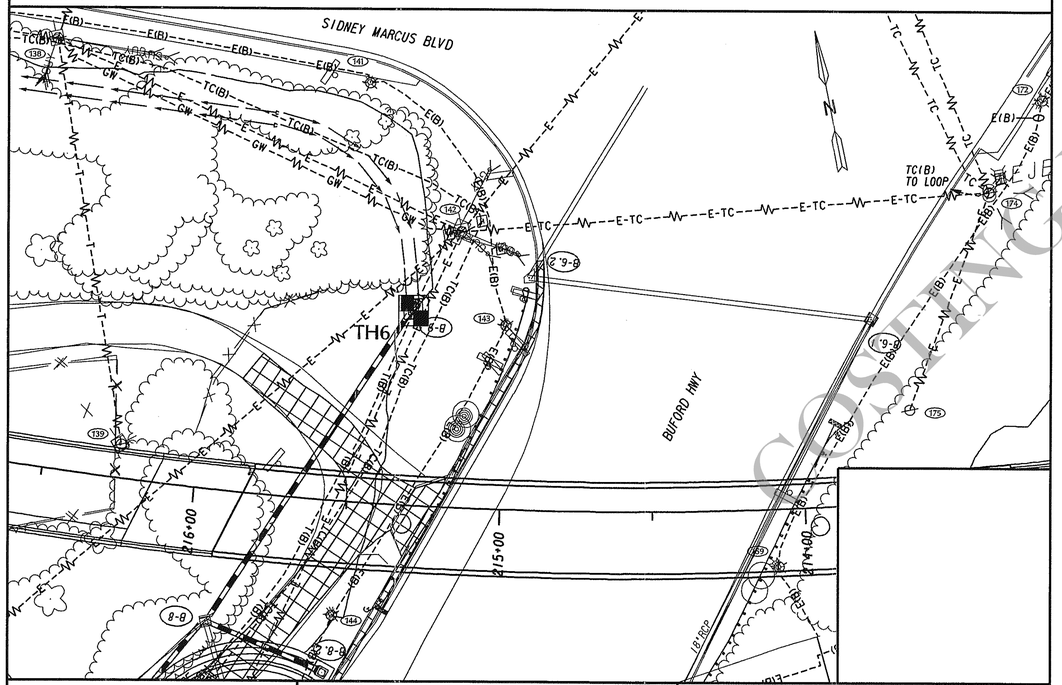

TBE GROUP PEACHTREE CORPORATE CENTER 6649 PEACHTREE INDUSTRIAL BLVD. SUITE J, NORCROSS GA 30092-4302 TELEPHONE: 678.421.0080	**CITY, COUNTY, STATE:** ATLANTA, FULTON, GA **GEN. LOCATION:** SIDNEY MARCUS/BUFORD HWY **PROPOSED:** I-85 @ GA400 CONNECTOR RAMPS **PLAN SHEET:** 24-13 **TEST HOLE STA./OFFSET:** 215+32/63' RT
	TBE PROJECT NUMBER: GA-069-001-00 **FOREMAN/TRUCK NO./FORM BY:** H. HOKSTAM/55-227/B. CRAWFORD **DATE:** 05/24/2010
	TH-06

CONTROL ACQUIRED BY GPS OR LOCAL SURVEY PROVIDED BY: TBE GROUP, INC.
HORIZONTAL DATUM: NAD'83(94 HARN)
VERTICAL DATUM: NAVD'88
UTILITY IN CONFLICT: UNKNOWN SIZE/TYPE BURIED ELECTRIC
UTILITIES FOUND: 2" POLYVINYL CHLORIDE BURIED ELECTRIC
CONDITION OF UTILITY(OBSERVED): GOOD
FIELD CONDITION: TALL GRASS
PAVING THICKNESS AND TYPE: N/A
CONDITION OF PAVING PRIOR TO WORK: N/A
PORTION OF PIPE EXPOSED FOR O.D. MEASUREMENT: ¾
REMARKS: N/A

CROSS SECTIONAL VIEW (FACING NORTHEAST)

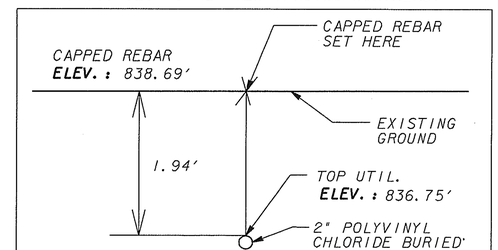

(TEST HOLE COORDS.)
N: 1390932.20
E: 2238806.48

NOTE: DEPTHS SHOWN WERE MEASURED, NOT CALCULATED.

SCALE IN FEET
0 50 100 150

PLAN VIEW

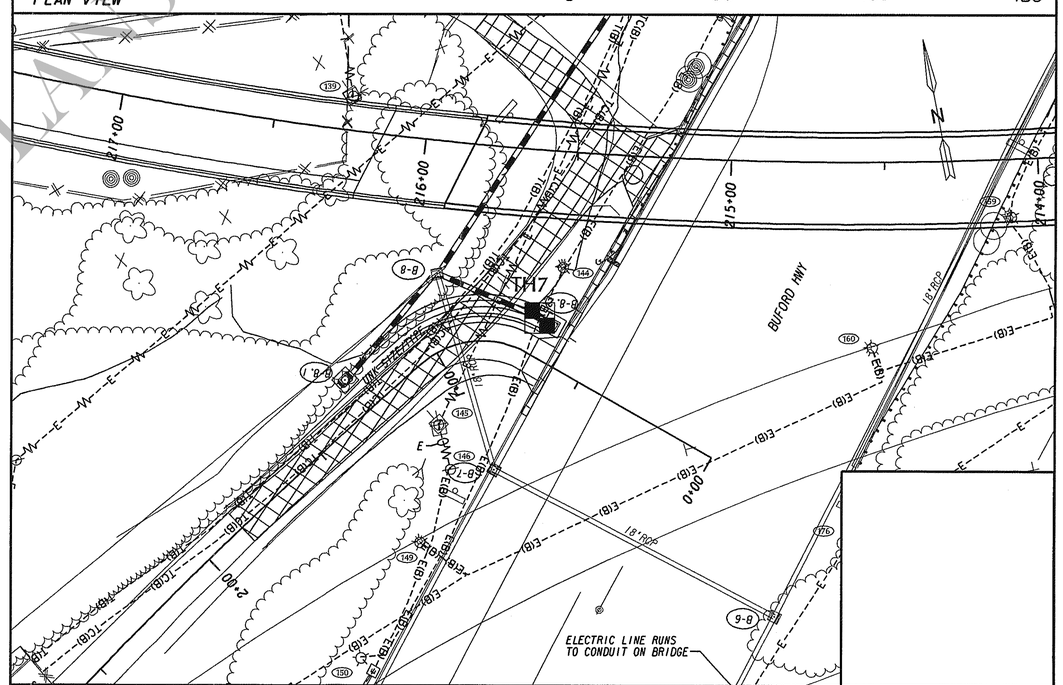

TBE GROUP PEACHTREE CORPORATE CENTER 6649 PEACHTREE INDUSTRIAL BLVD. SUITE J, NORCROSS GA 30092-4302 TELEPHONE: 678.421.0080	**CITY, COUNTY, STATE:** ATLANTA, FULTON, GA **GEN. LOCATION:** SIDNEY MARCUS/BUFORD HWY **PROPOSED:** I-85 @ GA400 CONNECTOR RAMPS **PLAN SHEET:** 24-13 **TEST HOLE STA./OFFSET:** 215+59/54' LT
	TBE PROJECT NUMBER: GA-069-001-00 **FOREMAN/TRUCK NO./FORM BY:** H. HOKSTAM/55-227/B. CRAWFORD **DATE:** 05/24/2010
	TH-07

COSTA PLANS

PLAN RELEASE			
DRAWN BY	DATE	CHECKED BY	DATE
BGC	06/18/10	RC	06/21/10
BGC	07/19/10	TWH	06/22/10
		RC	07/19/10

TBE PROJECT NUMBER
GA-069-001-00

TBE CONTACT
RANDY W. SANBORN, P.E.

TBE GROUP
PEACHTREE CORPORATE CENTER
6649 PEACHTREE INDUSTRIAL BLVD.
SUITE J, NORCROSS GA 30092-4302
TELEPHONE: 678.421.0080

REVISION DATES		

STATE OF GEORGIA
DEPARTMENT OF TRANSPORTATION
OFFICE: UTILITIES, JUN BIRNKAMMER, EIT

UTILITY PLANS

S.R. 400/ I-85
CONNECTOR RAMPS
P.I. NO. 762380-

DRAWING No. 24-0G

\762380UT0G.dgn 7/23/2010 9:54:16 AM
